



CARRIER COMMERCIAL SERVICE
5900 Northwoods Business Pkwy
Suite 8
Charlotte, NC 28269
(704)525-2644

Report of Eddy Current Inspection

Manufacturer: Carrier

Model: 30HXC136MY

Serial: 3208Q16316

Location: UNIVERSITY OF SOUTH CAROLINA
READINESS CENTER
SPARTANBURG, SC 29301

Inspected: January 29, 2019

Inspected By: JAMES A. PAGE, LEVEL III
TAI Services, Inc.

Reviewed By:



TECHNICAL MANAGER, LEVEL III

Table of Contents

Section A Inspection Report

 Part I Vessel Information

 Part II Support Bay Length

 Part III Comparison Graphs

 Part IV Summary of Inspection

 Part V Recommendations

 Part VI Data Sheets

 Part VII Tube Bundle Layout

 Part VIII Calibration Strip Charts

 Part IX Tube Strip Charts

 Part X Phase Charts

Section B Calibration Procedures

Section C Explanation of Abbreviations

Vessel Information

Manufacturer	Model	Style	Serial Number	Type
Carrier	30HXC136MY	Hermetic	3208Q16316	Screw

Condenser	
TestEnd	Left Hand Facing Control Panel
Tube Count	114
Tube Type	Cont. Fin IE w/Land
Tube Material	Copper
OD	.750
*NWT/Under Fins	.028
*NWT/Bell/Land	.049
#/Type Support	3 Mild Steel
Tube Numbering	Left to Right
Row Numbering	Top to Bottom
Tube Length +- 2	124 Inches


Evaporator	
TestEnd	Left Hand Facing Control Panel
Tube Count	109
Tube Type	Cont. Fin IE w/Land
Tube Material	Copper
OD	.750
*NWT/Under Fins	.028
*NWT/Bell/Land	.049
#/Type Support	3 Mild Steel
Tube Numbering	Top to Bottom
Row Numbering	Left to Right
Tube Length +- 2	124 Inches

Analyst: JAMES A. PAGE, LEVEL III

* Nominal Wall Thickness


Vessel Bay Length Information

**Condenser (Length = 124 inches)
S = Intermediate Support**



Bay 4	36.00"
Bay 3	37.00"
Bay 2	27.00"
Bay 1	24.00"

**Evaporator (Length = 124 inches)
S = Intermediate Support**



Bay 4	27.00"
Bay 3	24.00"
Bay 2	37.00"
Bay 1	36.00"

Summary of Inspection

An eddy current tube inspection was performed as part of a preventive maintenance program with the following results.

Condenser: 114 Tubes		
Tubes Tested: 114 Tubes		
Significant/Measurable Indications	Tubes Marked	Percent of Bundle
NO MEASURABLE DEFECTS		
Totals	0	.00

Evaporator: 109 Tubes		
Tubes Tested: 109 Tubes		
Significant/Measurable Indications	Tubes Marked	Percent of Bundle
NO MEASURABLE DEFECTS		
Totals	0	.00

Recommendations

An eddy current inspection was performed on the tubes in this machine. This test was performed using accepted eddy current test methods for the inspection of in-service tubing. It should be noted that Eddy Current is not a leak detection method. The possibility does exist that tubes could contain defects and/or leaks which are not detectable. If leaks are suspected, we recommend a pressure test be used to identify the leaking tubes.

The following suggested repair actions are based on accepted industry standards. After removing sample tubes to confirm the inspection results, a determination of corrective action should be made by the repair agency and end user. Only these parties have knowledge of the critical applications and long-term use of the equipment. If plugging is selected over replacement, both efficiency and capacity should be considered.

CONDENSER:

There were no measurable defects noted during this inspection.

EVAPORATOR:

There were no measurable defects noted during this inspection.

RE-INSPECTION RECOMMENDATIONS:

We recommend that a follow-up inspection be performed on these vessels as follows:

Condenser: 29 January 2022

Evaporator: 29 January 2022

A copy of this report should be retained in your files to be used for comparison at that time.

If you should have any questions concerning this report, or if we may be of further assistance, please feel free to call upon us.

Data Sheet




Location	Model	Serial Number	Date
UNIVERSITY OF SOUTH CAROLINA	30HXC136MY	3208Q16316	January 29, 2019
SPARTANBURG, SC 29301			

Row	Tube	Description	Area	Action Req.
		SET UP CALIBRATE & STARTED		
		CONDENSER 1/29/2019 12:34 pm		
		NO MEASURABLE DEFECTS		
		CALIBRATION CHECK & COMPLETED		
		CONDENSER 1/29/2019 01:17 pm		
		SET UP CALIBRATE & STARTED		
		EVAPORATOR 1/29/2019 01:25 pm		
		NO MEASURABLE DEFECTS		
		CALIBRATION CHECK & COMPLETED		
		EVAPORATOR 1/29/2019 02:19 pm		

Condenser Section

S/N 3208Q16316

Left Hand Facing Control Panel

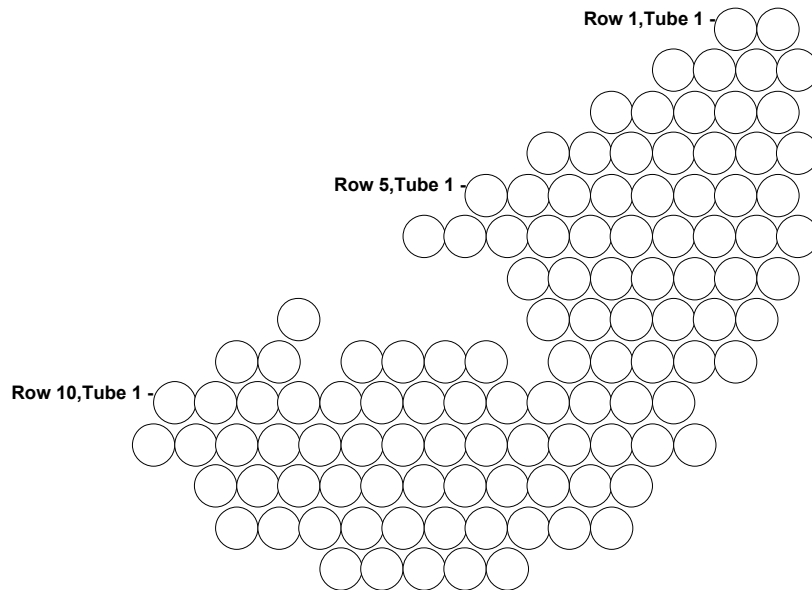



No Significant defects were found.

Evaporator Section

S/N 3208Q16316

Left Hand Facing Control Panel

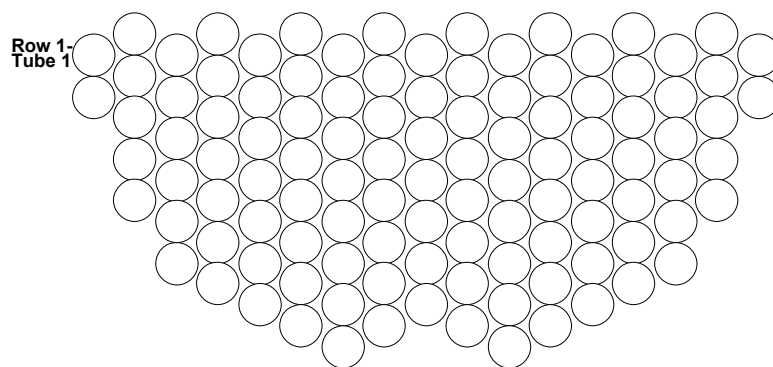


No Significant defects were found.

Calibration Page


Tube Type	Material	Nom Wall Thick	End Wall Thick	OD	Test Type	Probe Diameter
Cont. Fin IE w/Lan	Copper	.028	.049	.750	Cross/Diff	.5625

Condenser

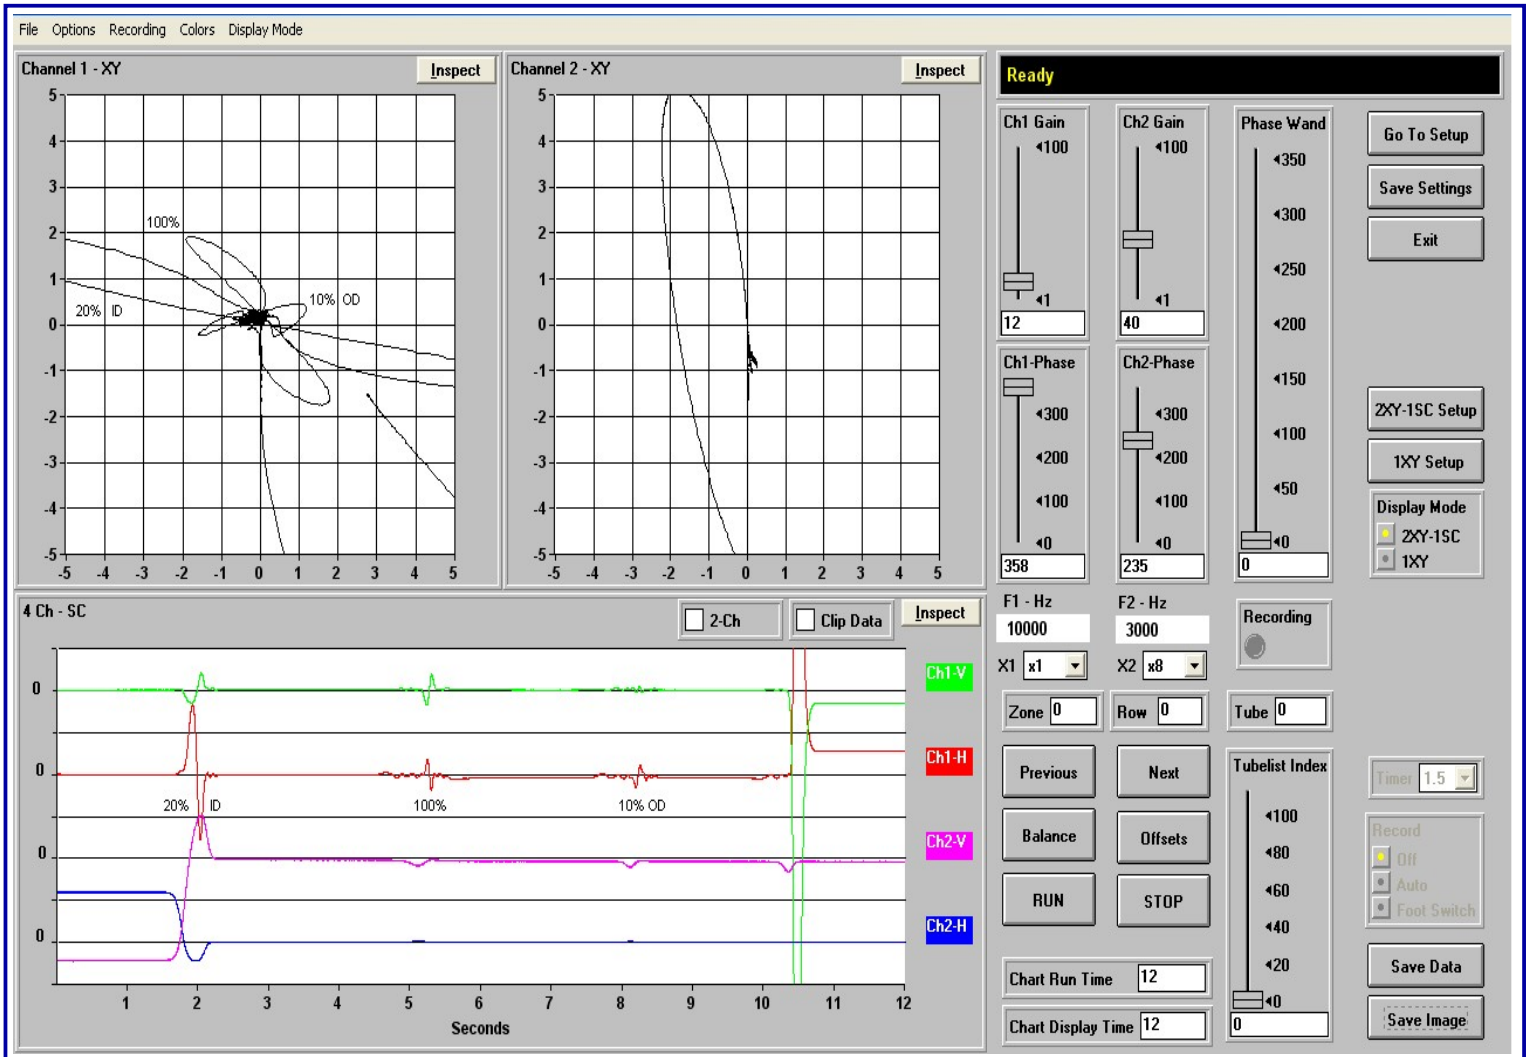


Note: Defects are compared to machined standards.
Actual Defect Geometry may differ.

Condenser Section

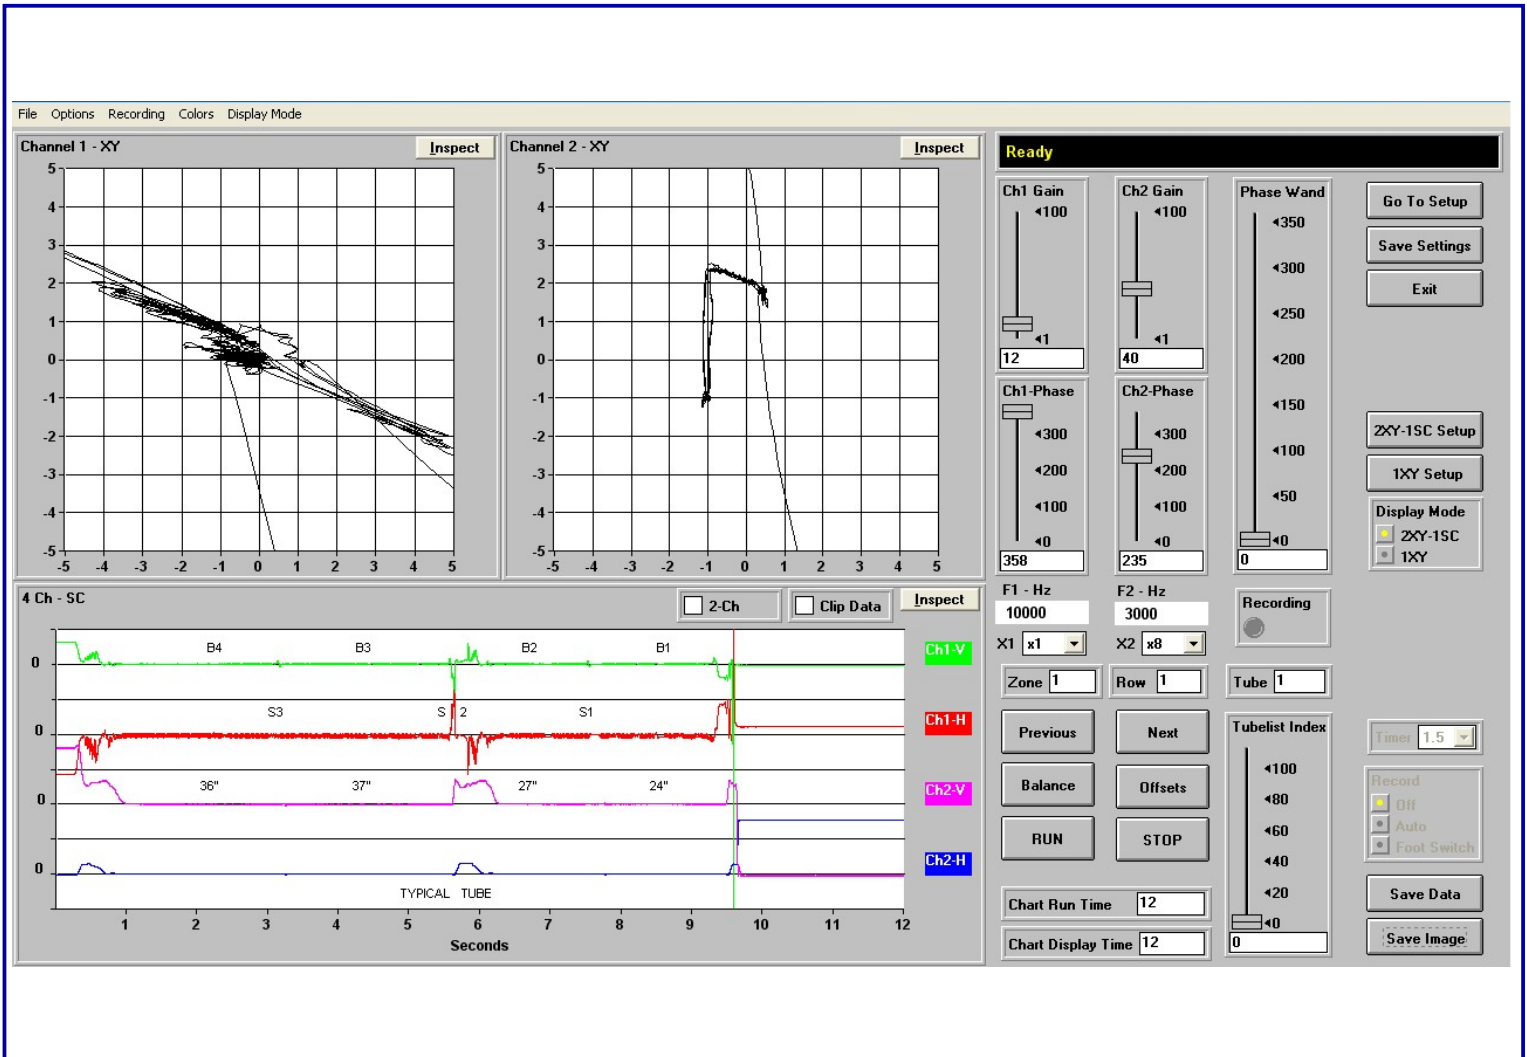


NO SIGNIFICANT DEFECTS (Row 1 Tube 1)

Condenser Section

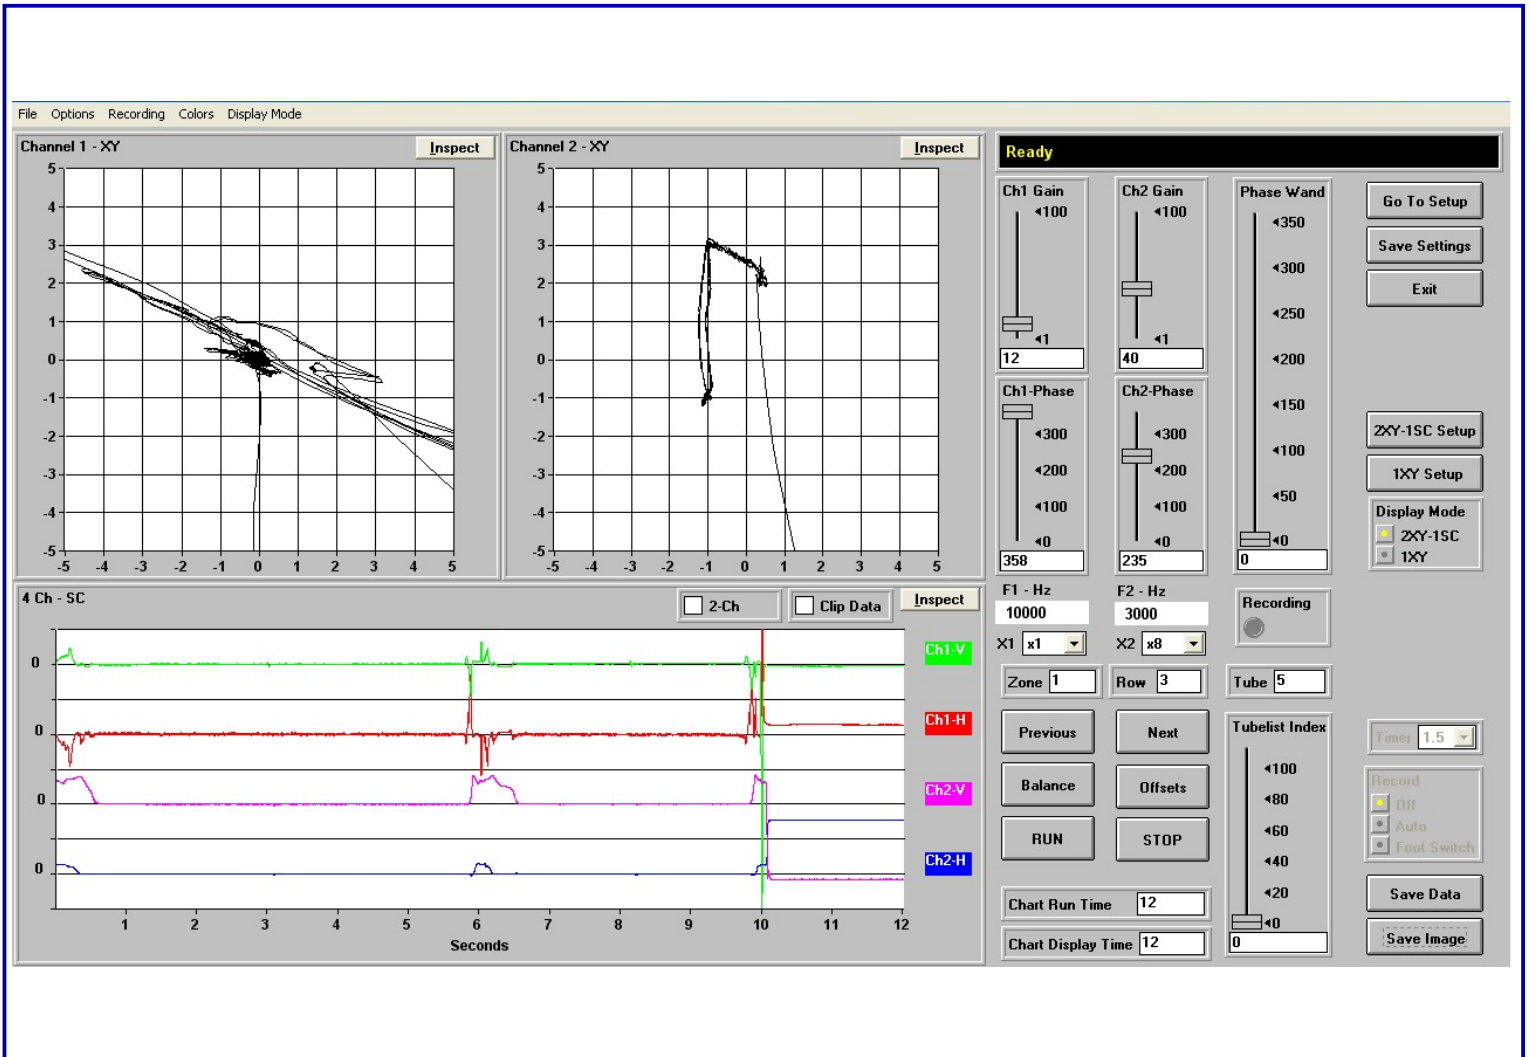


NO SIGNIFICANT DEFECTS (Row 3 Tube 5)

Condenser Section

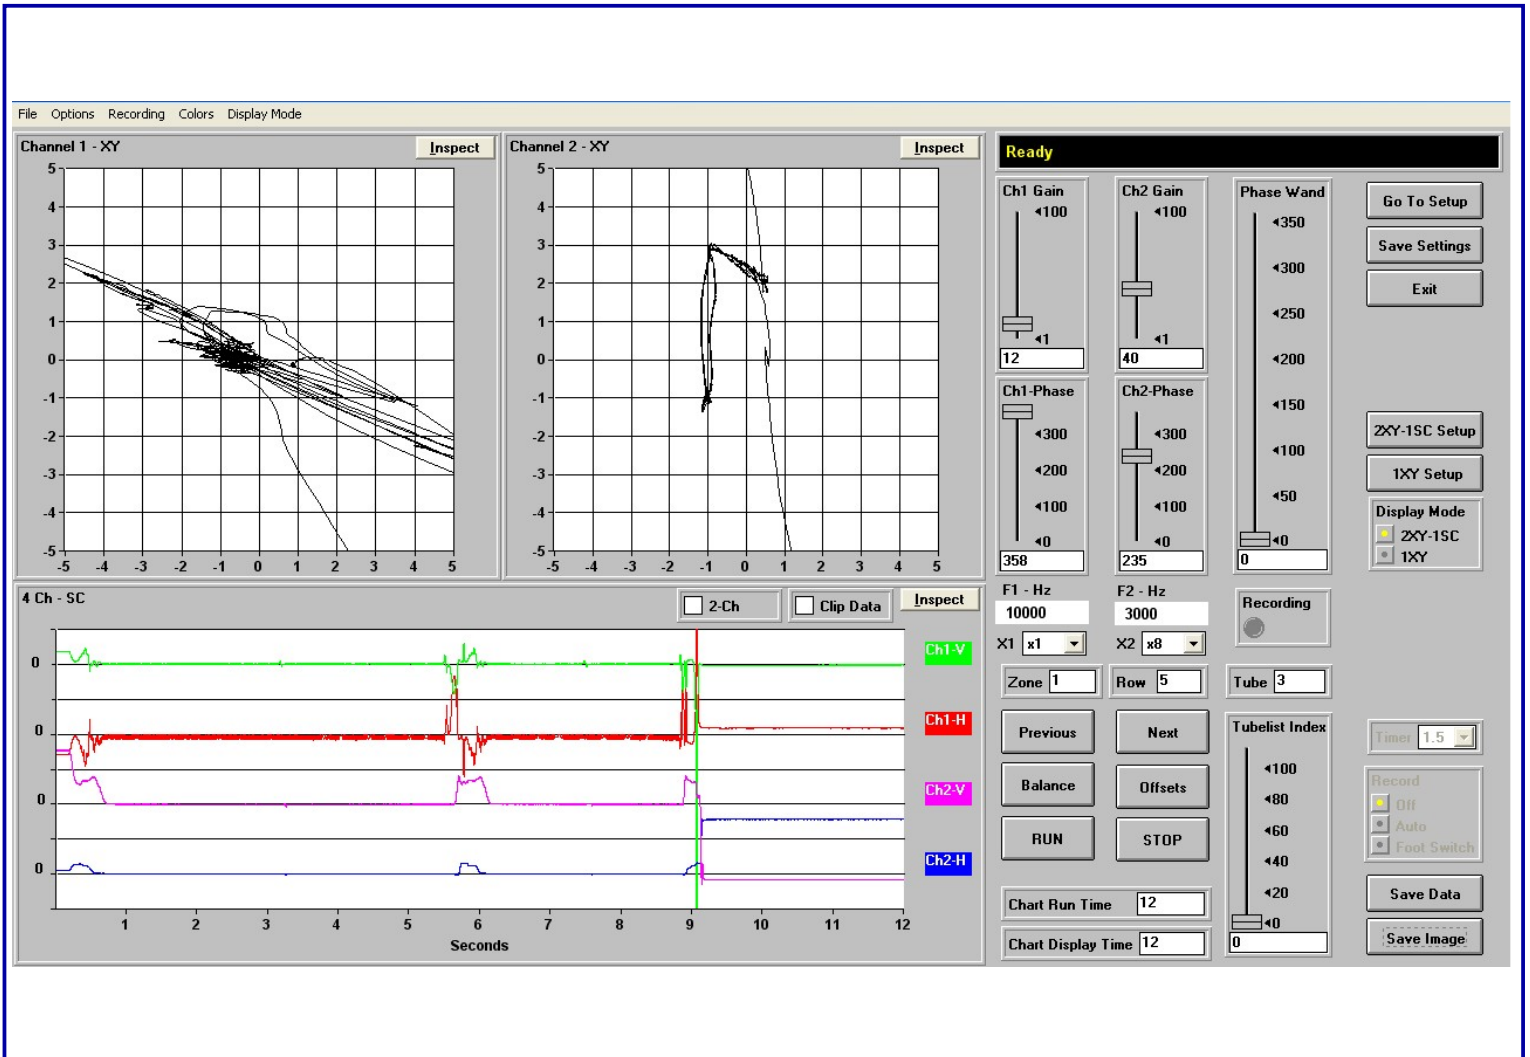


NO SIGNIFICANT DEFECTS (Row 5 Tube 3)

Condenser Section

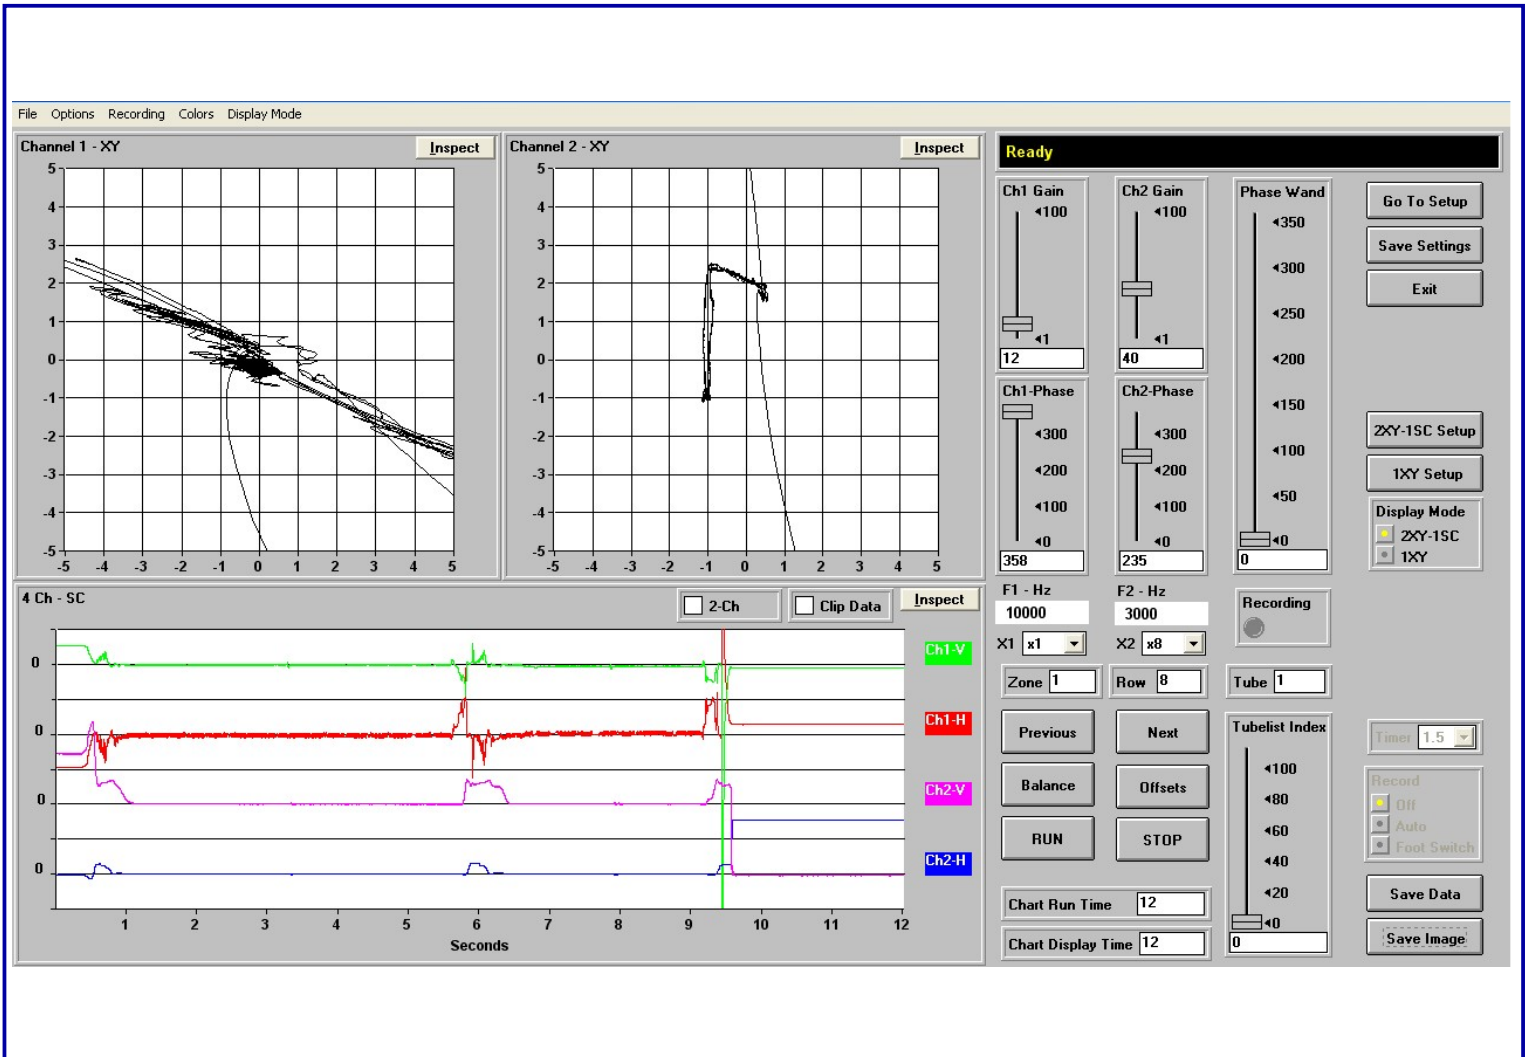


NO SIGNIFICANT DEFECTS (Row 8 Tube 1)

Condenser Section

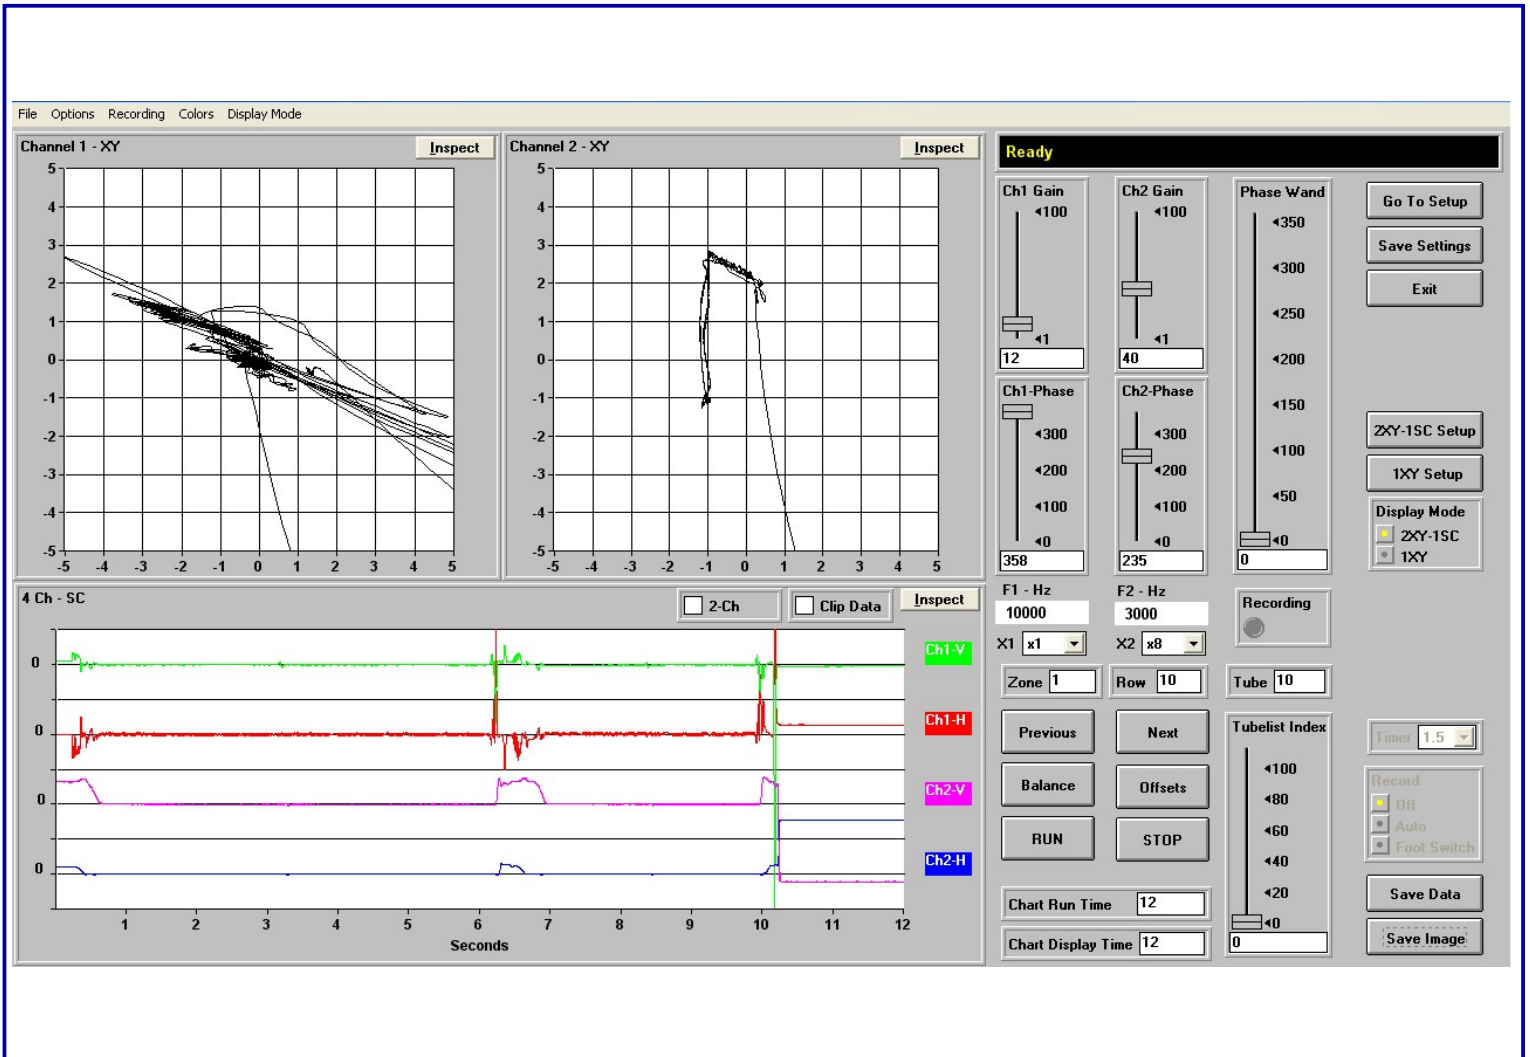

NO SIGNIFICANT DEFECTS (Row 10 Tube 10)

Condenser Section

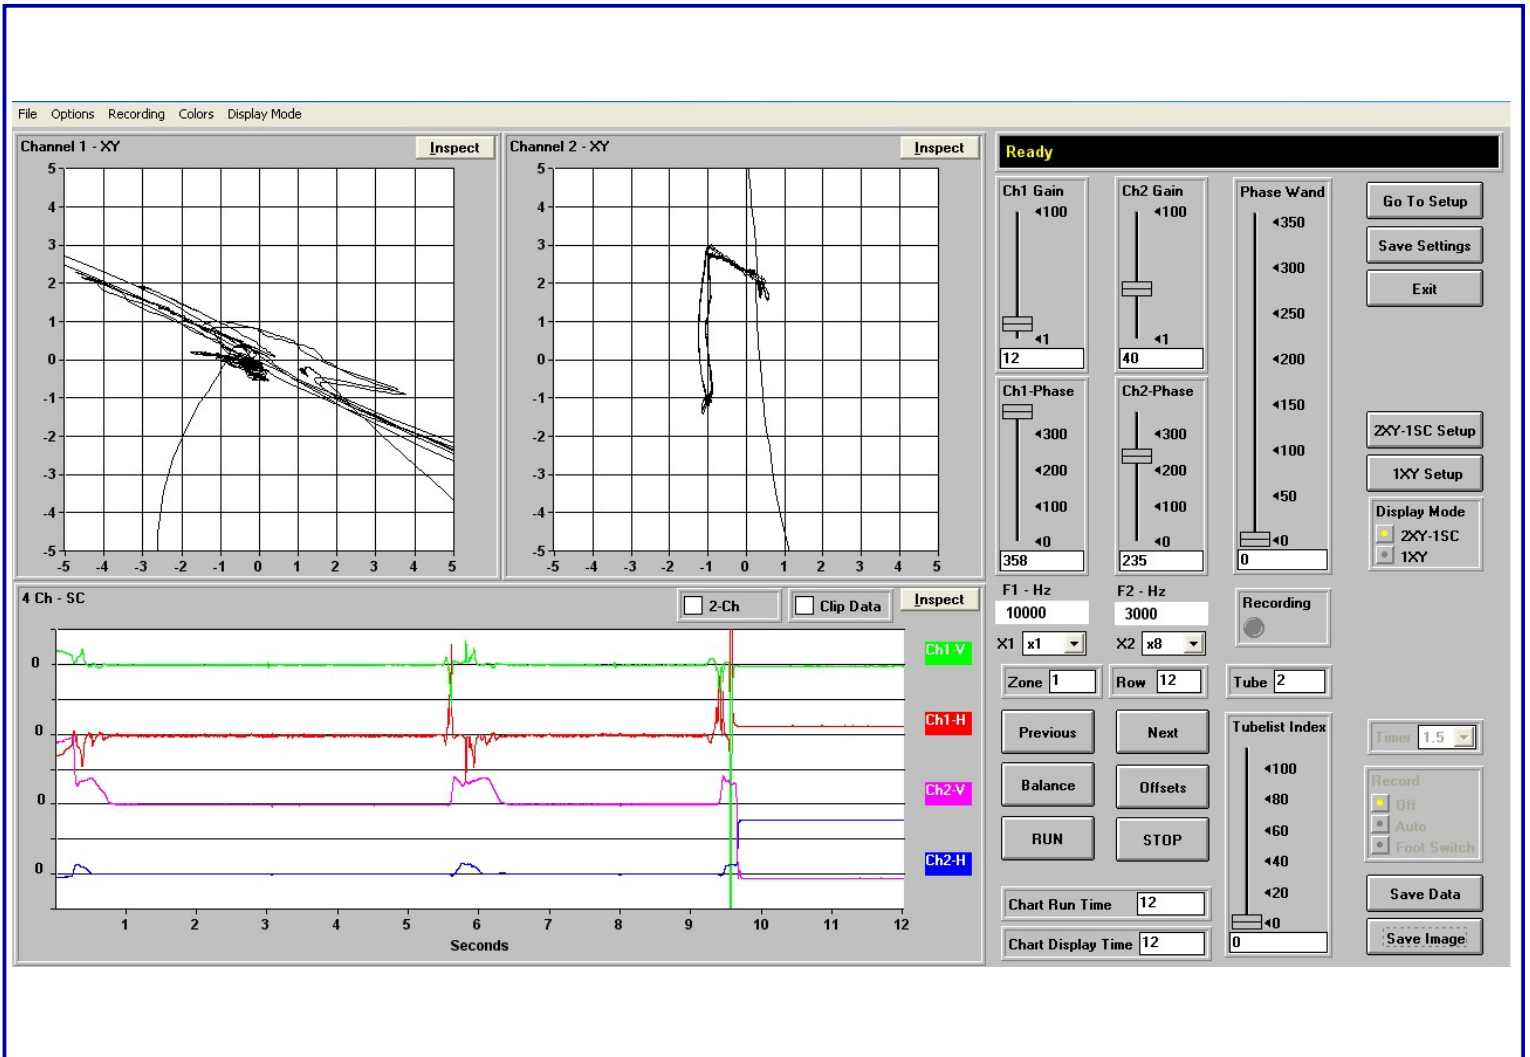


NO SIGNIFICANT DEFECTS (Row 12 Tube 2)

Calibration Page


Tube Type	Material	Nom Wall Thick	End Wall Thick	OD	Test Type	Probe Diameter
Cont. Fin IE w/Lan	Copper	.028	.049	.750	Cross/Diff	.5625

Evaporator

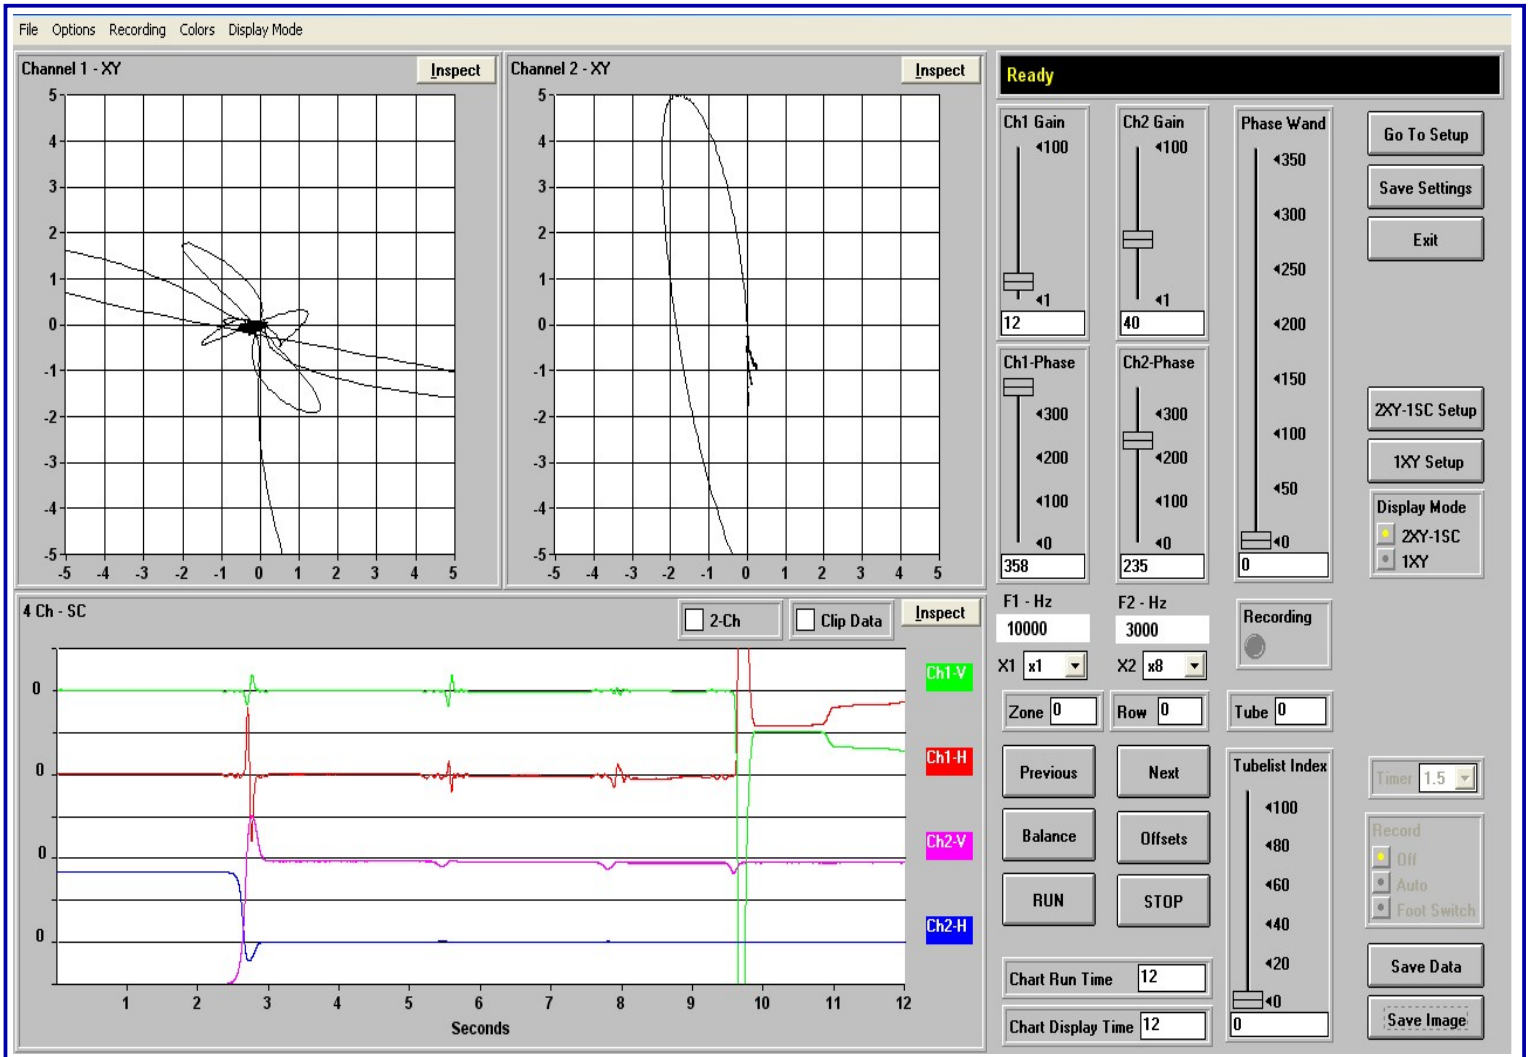


Note: Defects are compared to machined standards.
Actual Defect Geometry may differ.

Evaporator Section

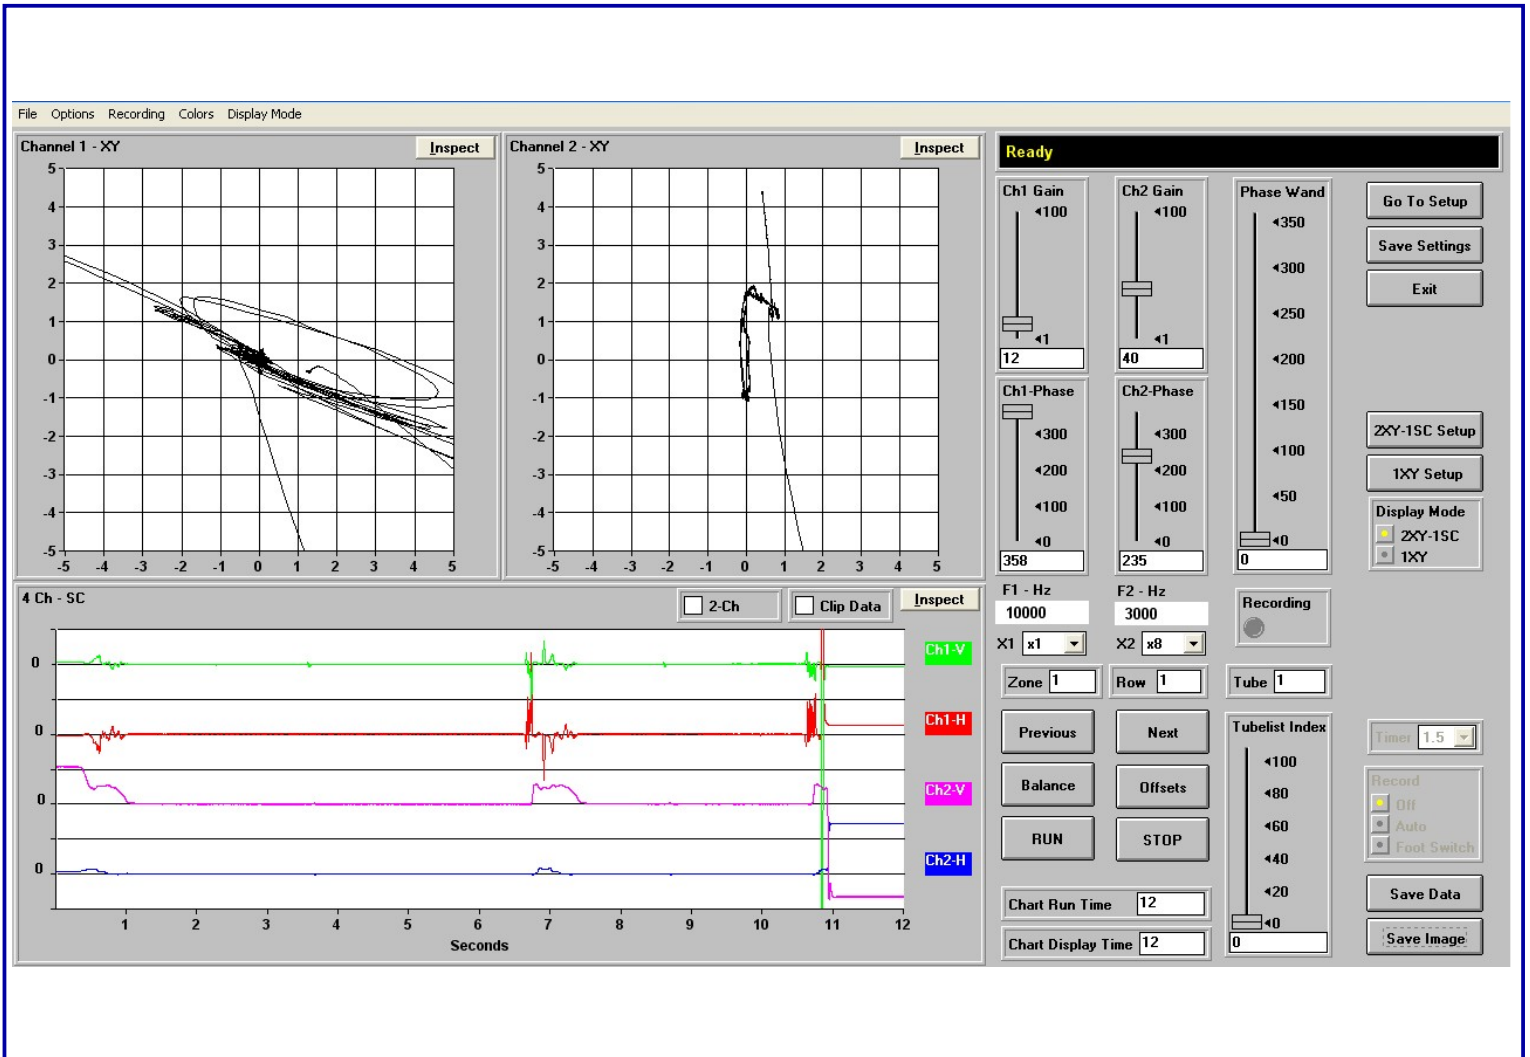


NO SIGNIFICANT DEFECTS (Row 1 Tube 1)

Evaporator Section

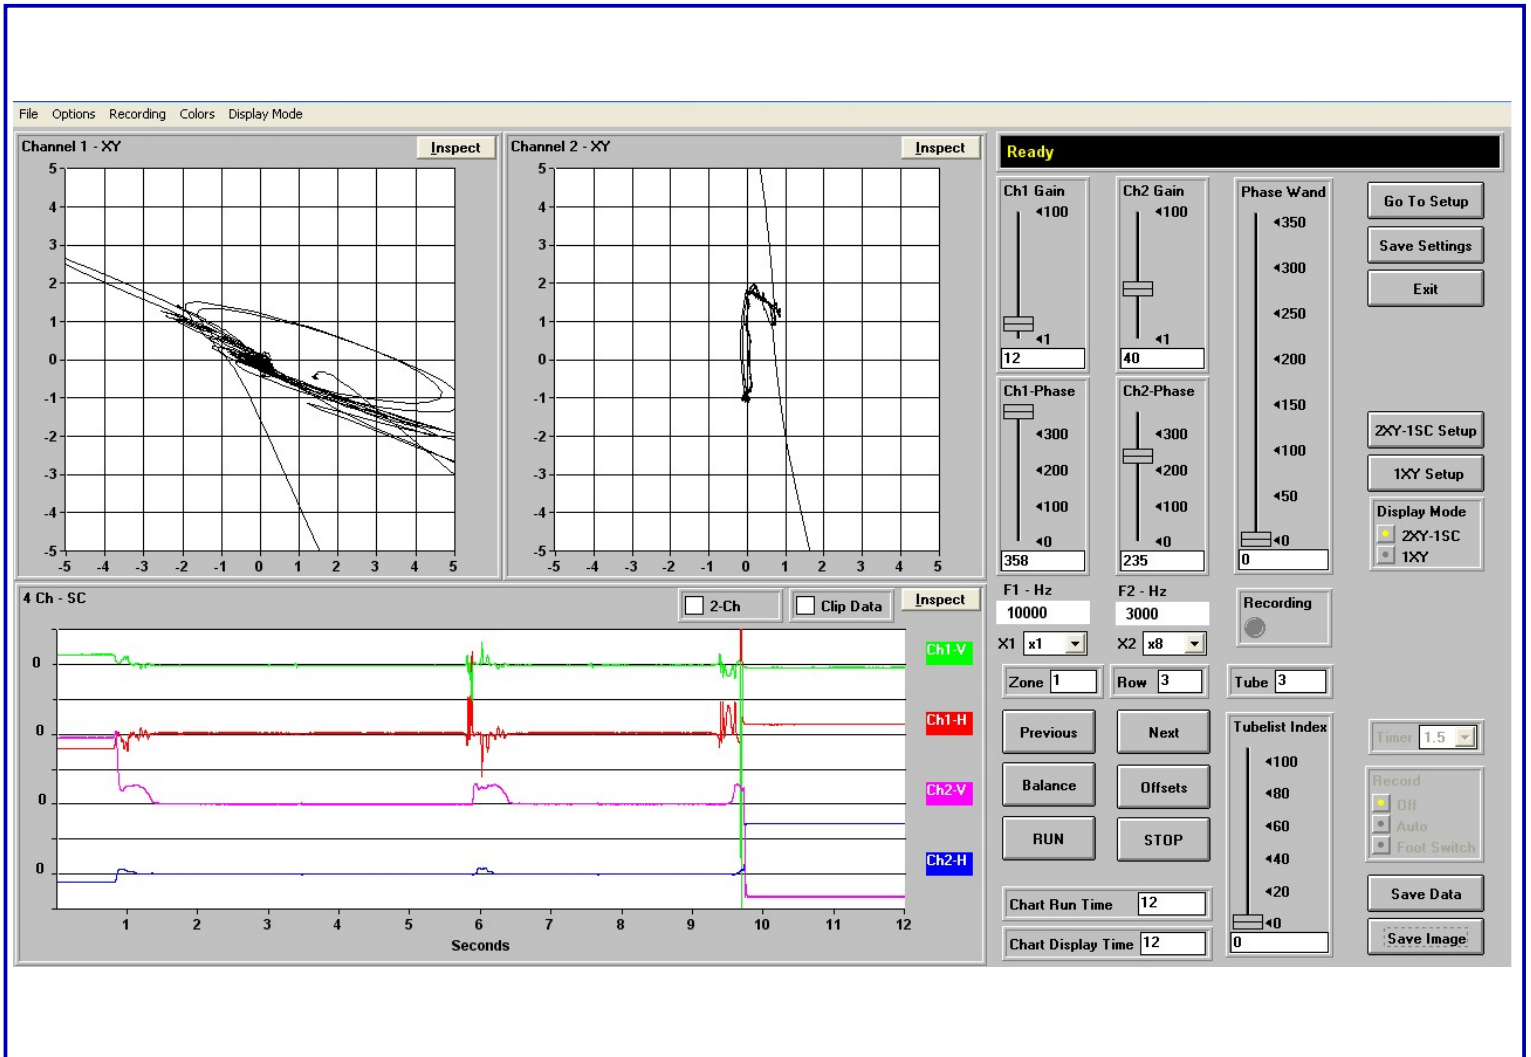


NO SIGNIFICANT DEFECTS (Row 3 Tube 3)

Evaporator Section

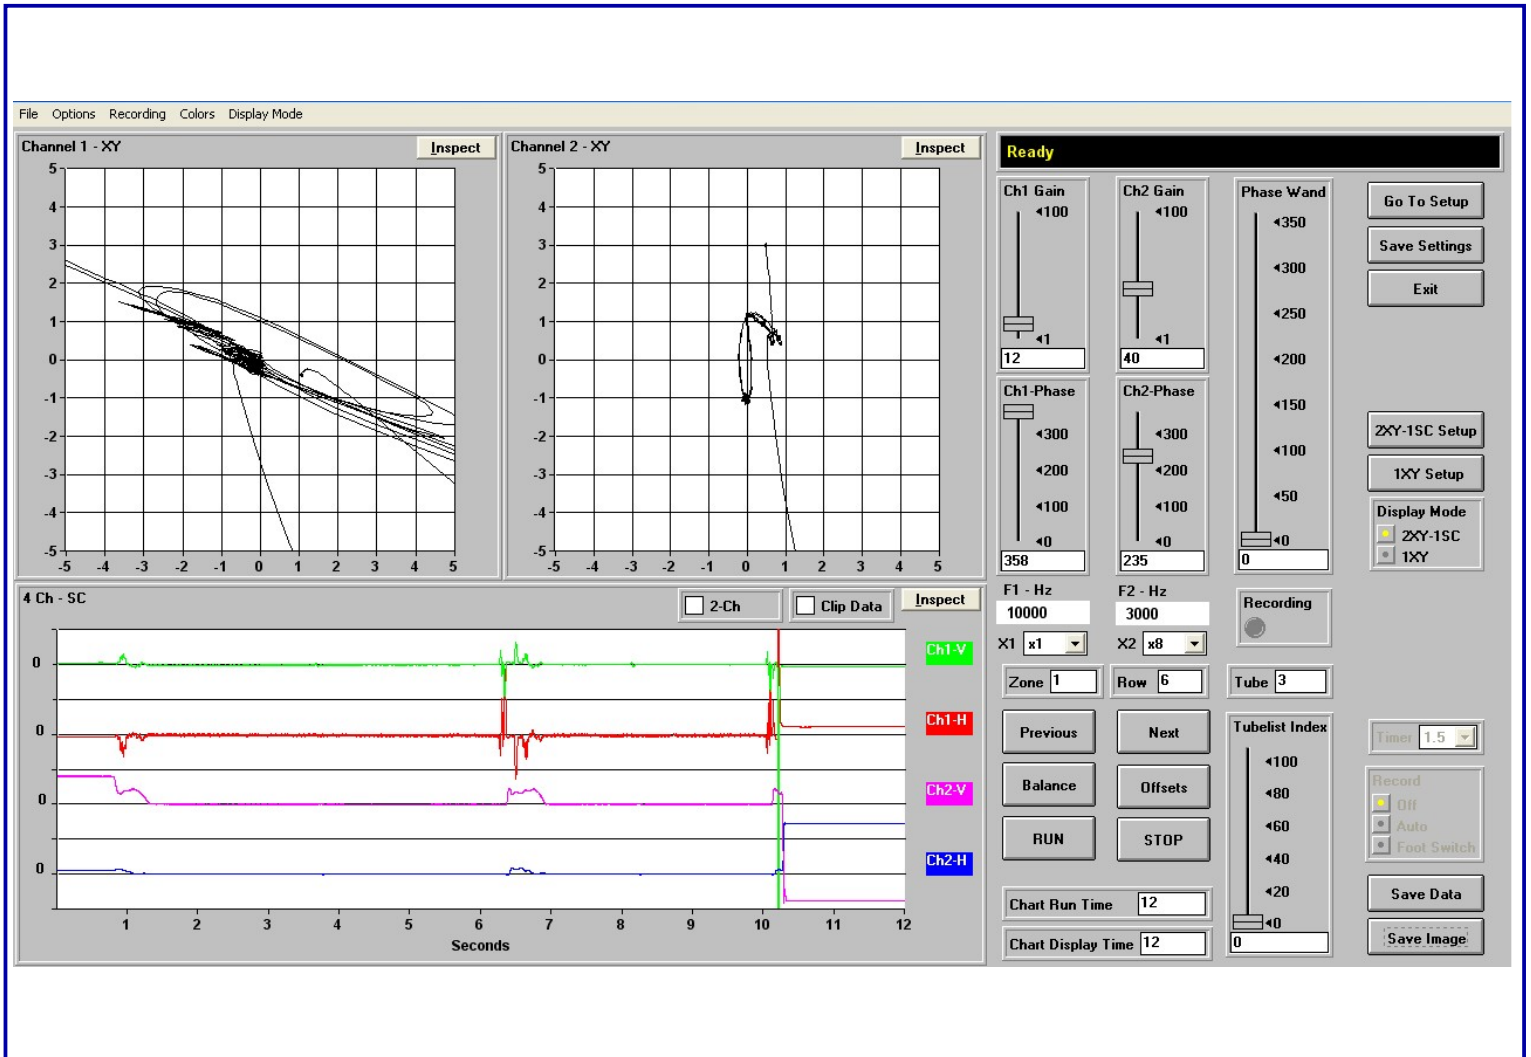


NO SIGNIFICANT DEFECTS (Row 6 Tube 3)

Evaporator Section

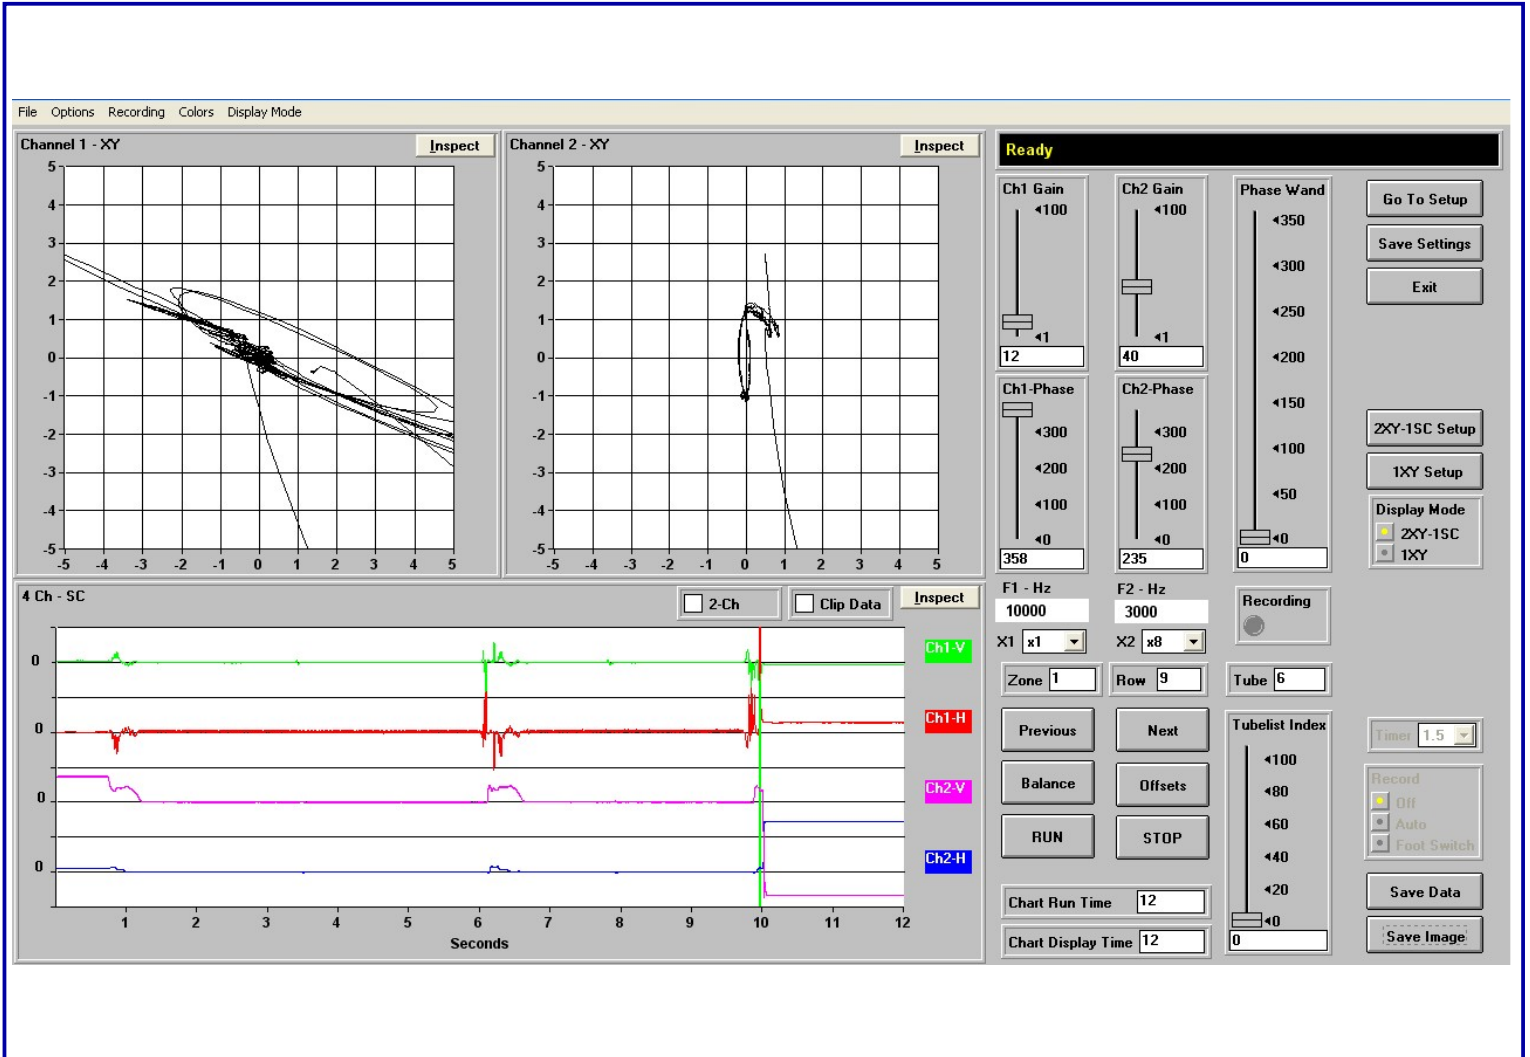


NO SIGNIFICANT DEFECTS (Row 9 Tube 6)

Evaporator Section

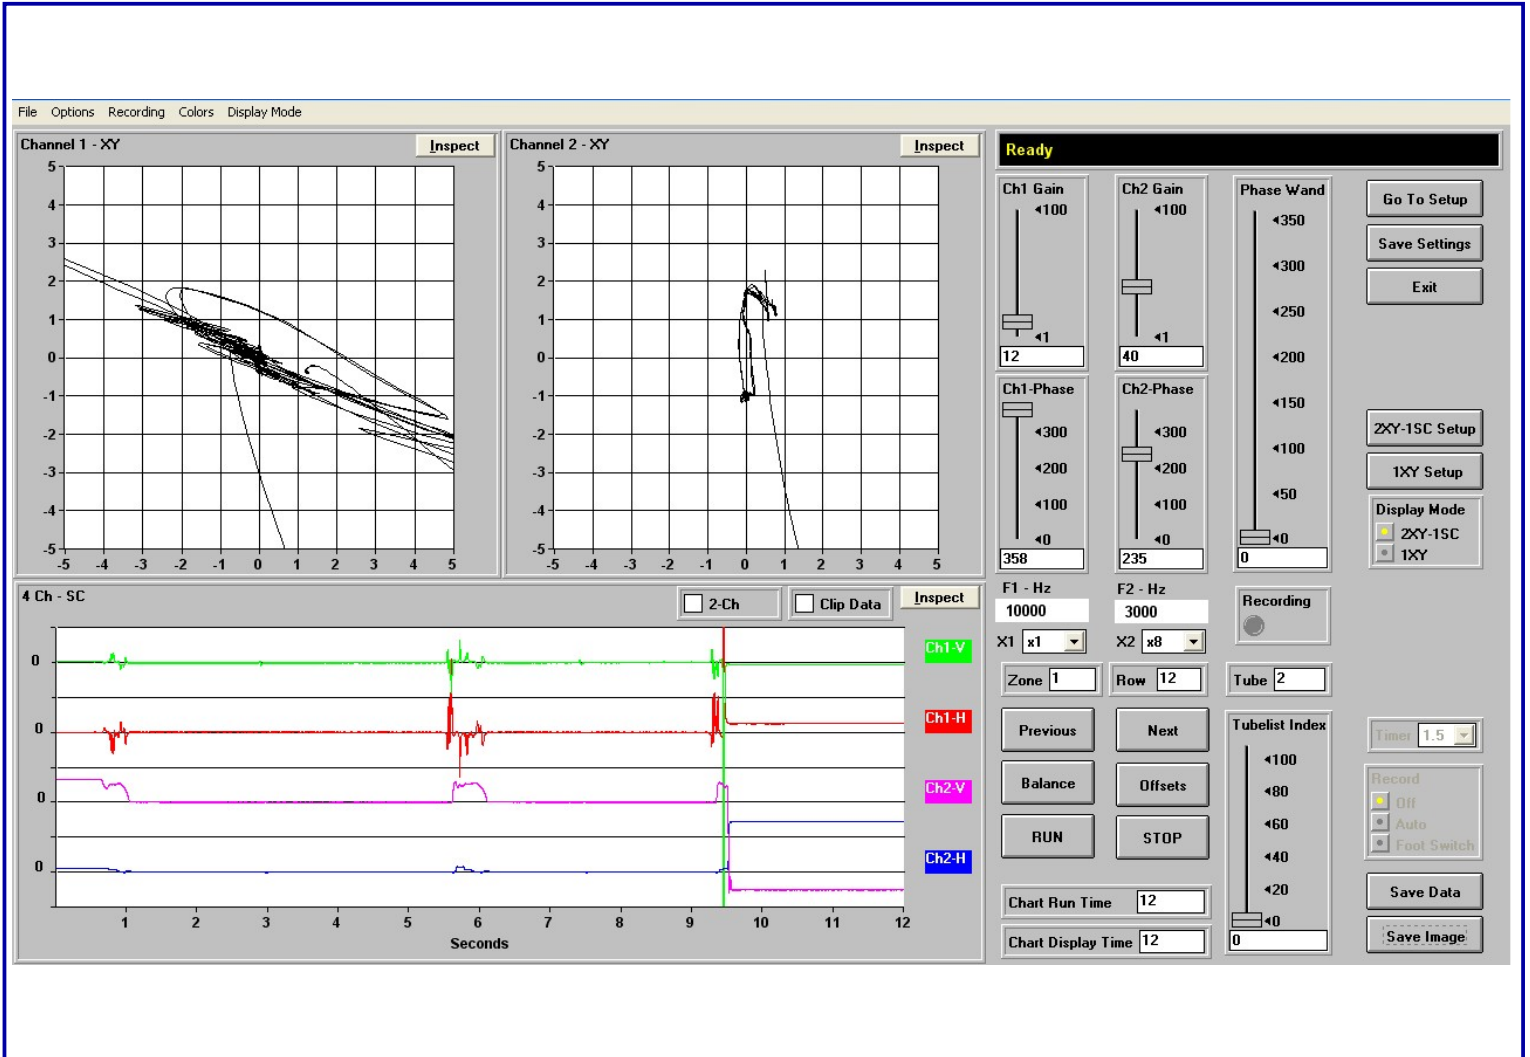

NO SIGNIFICANT DEFECTS (Row 12 Tube 2)

Evaporator Section

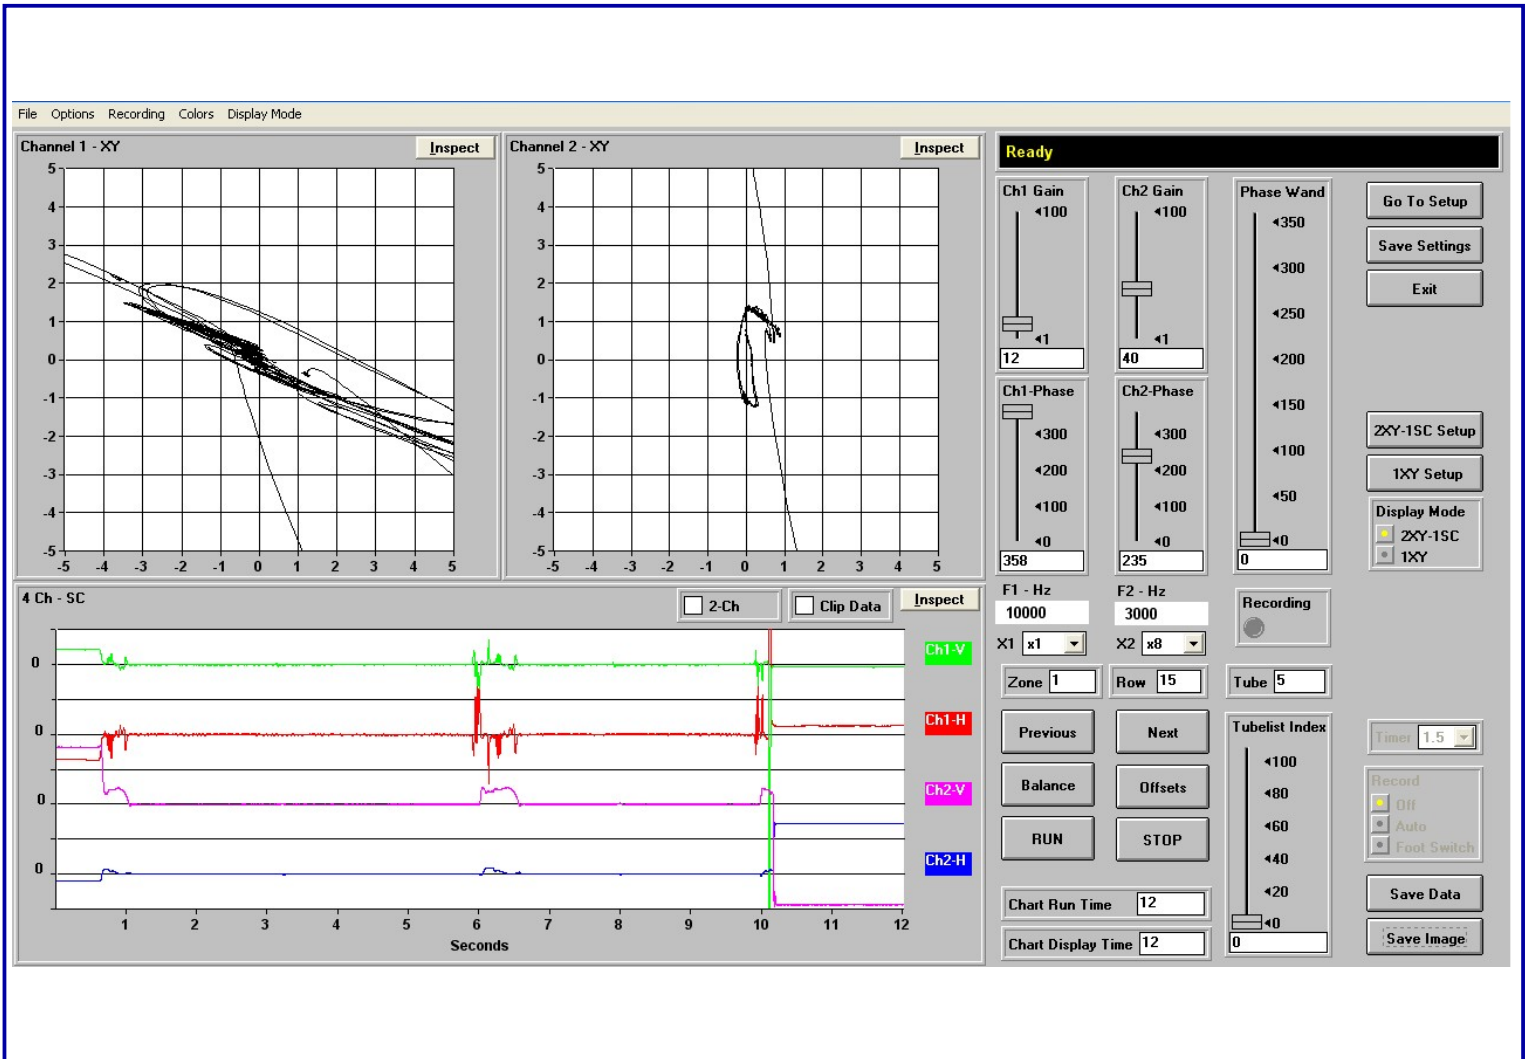

NO SIGNIFICANT DEFECTS (Row 15 Tube 5)

Calibration Procedure

A calibration procedure is performed prior to an inspection, and is repeated every 2 hours, or whenever improper operation of the test instrument is suspected. Test frequencies are selected prior to an inspection through experimentation to achieve optimum phase separation, and amplitude response for the tube type and alloy being inspected. An appropriate inspection probe is selected based on tube type, wall thickness, and alloy. The inspection probe will have a minimum fill factor of 80% through the smallest areas of the tubes being inspected. Instrument sensitivity is set high enough to determine background noise inherent in the tube and to produce a .05 Volt deflection for a .031 through wall hole at .25 V/Div.

Calibration Reference Standard

A Calibration Reference Standard representing a typical production run tube of the same alloy, tube type and nominal wall thickness is used to adjust test system response. The calibration reference standard used for the inspection of finned and internally enhanced tubing, has been milled in accordance with the American Society for Testing and Materials (ASTM). Standard Recommended Practices, E-243-80, E-426-76, and E571-76. The depth of the grooves and notches used for establishing instrument response are calculated to compensate for the influence of the fins and/or internal enhancements used on finned tubes. Where applicable, calibration reference standards are milled in accordance with the American Society of Mechanical Engineers (ASME), Section V, Article 8, Appendix I.

A strip chart recording of each calibration reference standard used for the inspection has been included in this report. Each artificial discontinuity has been identified on the strip chart recording.

Explanation of Abbreviations

Abbreviation	Explanation
ABN IND	Abnormal Indication
B	Bay
FB	Freeze Bulge
FBH	Flat Bottom Hole
FM	Foreign Material
ID	Internal Diameter
ID CORROSION	Internal Diameter, Corrosion
ID DEPOSIT	Internal Diameter, Deposit
ID PIT	Internal Diameter, Pit
IDML	Internal Diameter, Metal Loss
IE	Internally Enhanced
OD	Outside Diameter
ODML	Outside Diameter, Metal Loss
ODML@S	Outside Diameter Metal Loss at Support
OD DEPOSIT	Outside Diameter, Deposit
PLF	Possible Longitudinal Flaw
PRF	Possible Radial Flaw
PSC	Possible Stress Corrosion
S	Support
WAS	Wear at Support
>	Greater Than
<	Less Than
OTE	Opposite Test End
TE	Test End
